



STATE OF NEW YORK
OFFICE OF GENERAL SERVICES
DESIGN AND CONSTRUCTION GROUP
THE GOVERNOR NELSON A. ROCKEFELLER
EMPIRE STATE PLAZA
ALBANY, NY 12242



ADDENDUM NO. 2 TO PROJECT NO. 44362

CONSTRUCTION - PROJECT LABOR AGREEMENT PROJECT

**PROVIDE COMBINED SUPPORT MAINTENANCE SHOP
516 – ROUTE 216
STORMVILLE, NEW YORK 12582**

August 6, 2013

NOTE: This Addendum forms a part of the Contract Documents. Insert it in the Project Manual. Acknowledge receipt of this Addendum in the space provided on the Bid Form.

SPECIFICATION GROUP

1. 011000 SUMMARY OF THE WORK: Discard the Section bound in the Project Manual and substitute the accompanying Section (pages 011000 – 1 thru 011000 – 3) noted “Revised 8/6/2013”.
2. 013300 SUBMITTALS: Discard the Section bound in the Project Manual and substitute the accompanying Section (pages 013300 – 1 thru 013300 – 9) noted “Revised 8/6/2013”.

DRAWINGS

3. Addendum Drawing:
 - a. Drawing No. C-524 accompanies this Addendum and forms part of the Contract Documents.
4. Revised Drawings:
 - a. Drawing No. G-001, noted “REVISED DRAWING 08/05/2013” accompanies this Addendum and supersedes the same numbered originally issued drawings.
 - b. Drawing No. G-002, noted “REVISED DRAWING 08/05/2013” accompanies this Addendum and supersedes the same numbered originally issued drawings.

END OF ADDENDUM

James Dirolf, P.E.
Director of Design

SECTION 011000

SUMMARY OF THE WORK

PART 1 GENERAL

1.01 WORK COVERED BY CONTRACT DOCUMENTS

- A. The title and location of the Work is printed on the cover of this Project Manual.
- B. Type of Contract: Fixed price.

1.02 PROJECT LABOR AGREEMENT

- A. The work of this contract is to be performed as part of a Project Labor Agreement. The Project Labor Agreement (PLA) is included in the appendix of the specification.

1.03 SUBSTANTIAL AND PHYSICAL COMPLETION DATES

- A. Substantially complete the Work within 518 days after the Agreement is approved by the Comptroller.
 - 1. The time allocated for the performance of work under this contract includes 10 days for notification of the Contractor of the Comptroller's approval of the Agreement.
 - 2. The approval of the Agreement by the Comptroller constitutes the filing of the Contract Documents as a public record and notice to the Contractor that a fully executed contract exists between the Contractor and the State.
- B. Physically complete the Work within 30 days after the established Substantial Completion date.

1.04 CONTRACT AWARD SUBMITTALS

- A. Submittal No. 1 (Lead Contractor Only): Establish the subscription with the electronic submittals website provider as described in ELECTRONIC SUBMITTALS Article in Specifications Section 013300, and submit not later than 10 days after approval of the Contract by the Comptroller.
- B. Submittal No. 2: Submit the CONTRACTOR'S LIST OF SUBCONTRACTORS-SUPPLIERS INFORMATION REQUIRED IN SCHEDULES AND RECORDS Article in Specification Section 013000 not later than 15 days after approval of the Contract by the Comptroller.
- C. Submittal No. 3: Submit the CONTRACTOR'S PROGRESS SCHEDULE information required in SCHEDULES AND RECORDS Article in Specification Section 013000 not later than 15 days after approval of the Contract by the Comptroller.

1.05 RESTRICTED WORK PERIOD

- A. Do not perform the roofing and related Work between December 1st and April 1st unless approved otherwise, in writing, by the Director. During this period, clear the roof of materials, equipment, and debris. Maintain the roof in a watertight condition.
- B. Perform all tree removal between November 15th and March 31st. Tree clearing activities are limited due to the potential presence of the Federally-listed endangered Indiana Bat (*Myotis sodalis*) and the potential use of these trees as their summer habitat. The Indiana Bat is protected under The US Fish and Wildlife Service jurisdiction and the Endangered Species Act of 1973.
- C. See additional restrictions shown in specification section 310000 - Earthwork for Cold Weather Requirements.

1.06 ITEMS NOT INCLUDED

- A. The following items shown on the Drawings are not included in this Contract.
 - 1. Items indicated "NIC" (Not in Contract).

1.07 CONFINED SPACE

- A. Comply with confined space and permit-required confined space as defined in Title 29, Part 1910, Section 146 of the Code of Federal Regulations (29CFR 1910, 146).

1.08 REFERENCE SPECIFICATIONS AND STANDARDS

- A. Comply with the requirements of the various specifications and standards referred to in these Specifications, except where they conflict with the requirements of these Specifications. Such reference specifications and standards shall be the date of latest revision in effect at the time of receiving bids, unless the date is given.
- B. DOT Specifications: If the abbreviation DOT appears in these Specifications, it shall mean the most current edition of the New York state Department of Transportation, Office of Engineering specifications entitled "STANDARD SPECIFICATIONS – CONSTRUCTION AND MATERIALS", including all applicable Addenda in effect at the time of receipt of bids. The DOT specifications may be purchased from the Department of Transportation, Plan and Publication Sales, 50 Wolf Road, Albany, NY 12232, (518) 457-2124.

1.09 LAYING OUT

- A. Examine the Contract Documents thoroughly and promptly report any errors or discrepancies to the Director's Representative before commencing the Work.
- B. Lay out the Work in accordance with the Contract Documents.
 - 1. Layouts, which require the establishment of property lines or monuments, shall be performed by a Land Surveyor licensed by New York State.

1.10 SPECIAL INSPECTIONS

- A. Special inspections and tests are required by Chapter 17 of the Building Code of New York State (BCNYS). Inspections & Testing Services will be provided by the state unless otherwise noted.
- B. Contractors are responsible for notifying the Director's Representative regarding individual inspections listed in the **STATEMENT OF SPECIAL INSPECTIONS**. Contractors shall cooperate with the inspectors and testing agencies and sufficient notice and lead time (minimum 48 hours) must be allowed for inspection and testing to be performed.
- C. Where deficiencies are identified, the contractor must take corrective actions to comply with the contract documents or remedy the deficiencies in accordance with Article 9 of the General Conditions.

PART 2 PRODUCTS (Not Used)

PART 3 EXECUTION (Not Used)

END OF SECTION

SECTION 013300

SUBMITTALS

PART 1 GENERAL

1.01 RELATED REQUIREMENTS SPECIFIED ELSEWHERE

- A. Other requirements pertaining to submittals are included in the General Conditions and in the various sections of the Specifications.
- B. Administrative Requirements: Section 013000.
- C. Contract Closeout Submittals: Section 017716.
- D. LEED Documentation Requirements: 018113.

1.02 DEFINITIONS

- A. Deviation: Changes in products, materials, equipment and methods of construction from those required by the Contract Documents and proposed by the Contractor.

1.03 DEVIATIONS FROM REQUIREMENTS OF THE CONTRACT DOCUMENTS

- A. Deviations from the requirements of the Contract Documents will not be allowed unless a request for deviation is made in writing prior to or at the time of submission and the specific deviation is approved by the Director's Representative subject to the requirements of Article 4 of the General Conditions. The request for deviation shall be made utilizing the CONTRACT DOCUMENT DEVIATION REQUEST FORM (Form BDC 49) bound in the Appendix or from the OGS Web Site.
 - 1. The submission of a deviation shall be done in a timely manner according to the schedule of submittals to allow the Director sufficient time for review.

1.04 "OR EQUAL" TO BRAND NAME PRODUCTS

- A. Whenever a product is specified by brand name, a comparable brand, equal to that named, may be submitted for approval subject to the requirements of Article 5 of the General Conditions.
 - 1. The contractor shall bear the burden of proving that the proposed product is equal to the specified product. The submission of an "or equal" shall be done in a timely manner to allow the Director sufficient time to review the proposed product.
 - 2. Whenever a color or pattern is indicated by a specific manufacturer's name or number, the intent is to communicate the required color or pattern of the material. Other manufacturers' comparable colors or patterns may be submitted for approval as equal.

1.05 WAIVER OF CERTAIN SUBMITTAL REQUIREMENTS

- A. Unless otherwise specified, the requirement to submit product data and samples for approval will be waived for products specified by brand name if the specifically named products are furnished for the Work. In such cases, submit required Product Data to the Director's Representative via the Submittals Website for information only.

1.06 ADMINISTRATIVE AND COST REQUIREMENTS

- A. The Contractor shall include the full cost of an internet web-based submittals service (Submittals Website) to transmit and track project related documents including the documents of all related contracts. Include the costs and/or fees of the Submittals Website subscription in the Contract Amount. Contact service provider to verify cost prior to bid.
The Contractor shall:
 - 1. Not later than 5 days after Award, execute the form of agreement with the Submittals Website System Vendor and shall have notified the Director's Representative and the related work contractors of agreement.
 - 2. Not later than 15 days after Award provide the Submittal Website with all required information from Project Manual in regard to set up of the Submittal Website and ensure it is fully ready for use.
 - 3. Not later than 15 days after Award provide proof of payment from the vendor including OGS project number and other relevant data.
 - 4. Provide the Submittals Website project subscription in the name of, and administered by the Director's Representative.
 - 5. Provide the Director's Representative and primary design consultant full control over required items list and access to edit, add or remove items during project.
 - 6. Submit at completion of the project a minimum four sets of archival discs that include all documents and tracking logs in a navigable format shall be sent by system vendor to Director's Representative. Acceptable archive formats include the following: CD, DVD, USB flash drive or downloadable link.
- B. Identify all submittals by project title and number. Include Contractor's name, date, and revision date. On shop drawings, product data and samples, also include the name of the supplier and subcontractor (if any), and applicable specification section number. Stamp each submittal and initial or sign the stamp to certify review and approval of submittal.
- C. Assemble submittals in accordance with the requirements in the individual sections of the Specifications and as required by this section. It is the Contractor's responsibility to review and verify that all information required for each submittal is included in the submittal package. Errors or omissions found by the Contractor are to be corrected prior to the submission of the submittal package for approval. Incomplete submittal packages that have been submitted for review and approval will be returned.
 - 1. It is the Contractor's responsibility to verify that portions of the submittal package to be provided by a subcontractor (or supplier) are complete, as

well as portions of the submittal package being provided directly by the Contractor.

2. Do not combine the submittals of more than one specification section with submittals required by other specification sections unless specifically stated in the contract specifications.
- D. If a submittal is based on, or the result of, a change order or field order to the Contract documents, include copies of the applicable change order or field order with the submittal.
- E. The Contractor shall employ or otherwise provide a full-time Submittal Coordinator for no less than 90 days after the Initial Job Meeting (IJM). The Submittal Coordinator shall have regularly been engaged in construction administration for a minimum of 3 years and shall not be employed or otherwise engaged as the Project Manager or Superintendent for either the Work of this Contract or be employed in any role, full or part time, outside of this Contract.

1.07 SUBMITTALS

- A. Product Data: Proof of payment not later than 15 days after Award.
- B. Submittal Coordinator Qualifications: not later than 10 days after Award. Include resume and references, and other certification, licenses, or other requested information.

1.08 RE-EVALUATION FEE

- A. In accordance with Article 4.7 of the General Conditions, a re-evaluation processing fee will be levied against the Contractor for each re-evaluation of any Submittal Package submission that was returned for failure to comply with the submittal requirements relative to completeness, content or format.

1.09 ELECTRONIC SUBMITTALS

- A. A Submittals Website, an internet (web-based) service shall be used to provide an on-line database and repository which shall be used to transmit and track project related documents. The intent for using the Submittals Website is to expedite the construction process by reducing paperwork, improving information flow, and decreasing submittal review turnaround time.
 1. Project submittals (shop drawing, product data and quality assurance submittals) shall be transmitted by the Contractor in Portable Document Format (PDF) to the Submittals Website, where it will be tracked and stored for retrieval for review. After the submittal is reviewed it is uploaded back to the Submittals Website for action or use by the Contractor and Director's Representatives.
 2. The service also tracks and stores documents related to the project such as RFI's (Request for Information), IB's (Information Bulletins), CAD Coordination, Minutes, Testing, Closeout, and SWPPP documents.
- B. For each submittal, the Contractor shall review and apply electronic stamp certifying that the submittal complies with the requirements of the Contract

Documents, including verification of manufacturer/product, dimensions and coordination of information with other parts of the work.

- C. It is the Contractor's responsibility to provide the submittals in a PDF format. The contractor may use any of the following options:
1. Subcontractors and suppliers provide electronic submittals in PDF format to the Contractor via the Submittals Website.
 2. Subcontractors and suppliers provide paper submittals to the Contractor, who electronically scans and converts them to PDF format.
 3. Contract a Scanning Service, which will allow the Contractor and the Contractor's subcontractors and suppliers to provide paper submittals to the Scanning Service, which electronically scans and converts them to PDF format. It will be the Contractor's responsibility to transmit the scanned submittals to the Submittals Website.
- D. Image Quality:
1. Image resolution: The PDF files shall be created at a minimum resolution of 200 dots per inch utilizing the original document size. The Contractor will be responsible to increase the resolution of the scanned file or images being submitted as required to adequately present the information.
 2. Image Color Rendition: When information represented requires color to convey the intent and compliance, provide full color PDF reproduction.
- E. Internet Service and Equipment Requirements:
1. The Contractor will be required to have an Email address and Internet access at Contractor's main office.
 2. Unless the Contractor will exclusively be using a Scanning Service to create all PDF documents, the Contractor will be required to own a PDF reviewing, creating and editing software, such as Adobe Acrobat (www.adobe.com), Bluebeam PDF Revu (www.bluebeam.com), or other similar PDF reviewing, creating and editing software for applying electronic stamps and comments.
- F. Training and Support:
1. Web-based training and support shall be available, free of charge from the Submittals Website, for all project participants regarding use of the Submittals Website and PDF submittals.
 2. Coordinate training schedule through the Director's Representative.
- G. Products:
1. Basis of specification is Submittal Exchange, 800-714-0024, www.submittalexchange.com.
 2. If a Pre-Award Meeting is held, it may include discussion regarding conformance of the Contractor proposed Submittal Website based on the criteria established below.
 3. Submit documented conformance and provide an online demonstration to the Director's Representative within five days of Award of Contract if a product other than Submittal Exchange is proposed.
 4. Acceptable Submittal Website shall document conformance with the following requirements:

- a. Independently hosted, web-based system for automated tracking, storage and distribution of contract submittals and other contract related documents. FTP sites, e-mail exchanges, and server-based systems hosted from inside a contractor's office will not be considered.
- b. Utilize 256-bit SSL encryption and hosted at SAS70 Type II compliant data centers.
- c. Minimum four years experience of use on comparable commercial construction projects. "Comparable commercial construction projects" shall include documented use on a minimum of twenty governmental or public-entity projects of ten million dollar construction value or greater.
- d. Website requirements:
 - 1) Minimum of four years documented 99.5% website uptime.
 - 2) Minimum of four gigabytes of on-line storage available for each contract, for storage of all documents related to that contract.
 - 3) Minimum of two gigabytes of on-line storage for common documents relating to all contracts for the project.
 - 4) Redundant storage of all project information (all contracts) at a minimum of two geographically separate storage sites (not in the same building).
- e. Unlimited secure individual user accounts and system access for all project subcontractors, prime contractors, OGS staff, design consultants, and subconsultants.
- f. Separate locations for OGS staff, design consultant, and subconsultant review comments with contractors restricted from viewing comments until final review or release by OGS staff or primary design consultants.
- g. Full version histories and dates of exchanges automatically tracked and available for viewing, searching, and reporting in a linear log format compatible with the Design and Construction Schedule of Submittals.
 - 1) Each Contract's Submittal Log shall be tracked and maintained independent of the Submittal Logs of the related Contracts.
 - 2) Each Contract's Submittal Log shall identify and highlight long lead items and critical submittals.
- h. Automatic, email reminders of past due items to related reviewers by specification and discipline.
- i. Customized, automated PDF form generation matching OGS standard templates for Transmittal, IB, RFI, and Design & Construction Submittal Comment forms. Documentation and demonstration of automatic form generation using OGS templates must be submitted for approval.
- j. Automated workflow processes
 - 1) Two stage review workflows for Submittal, and RFI,
 - 2) Posting Only for IB, CAD Coordination, Minutes, Testing, Closeout, and SWPPP documents.

- 3) Documentation of automated workflow processes matching requirements must be submitted for approval.
 - k. Functionality to group submittals as required packages and apply forms and review comments to entire package simultaneously.
 - l. System vendor shall provide minimum one-hour live web meeting training sessions to prime contractors, design consultants, subconsultants, and OGS staff prior to project start.
 - m. System vendor shall make available minimum thirty-minute live web meeting training sessions for subcontractors at least once weekly for the entire duration of the project.
 - n. System vendor shall provide access for OGS staff, design consultants, subconsultants, prime contractors, and subcontractors to live technical support by phone and email minimum of 8 AM to 5 PM EST on standard business days for the entire duration of the project at no additional cost.
 - o. During the project, the system shall allow the Director's Representative to have the ability to download project data periodically at key milestones.
- H. Paper prints (hardcopies) of reviewed submittals:
- 1. Record Copy: Within 14 days of receipt of submittals marked "Approved", "Approved As Noted", or meeting the requirements of Article 1.05 of this specification section, each Contractor shall provide one paper copy of the submittal they are responsible for to the Director's Representative.
 - a. Paper copies shall be printed in a size format equal to the original document.
 - b. Scaled Shop Drawings shall be printed to the scale noted on the drawings.
 - c. The resolution of the printed copy shall be equal to that of the PDF file that it is being printed from.
 - d. The Record Copy shall be used by the Director's Representative during the construction of the project and shall be retained as a turn-over item to the facility at the end of the project as required section 017716 Contract Closeout.
 - 2. Contractor Copies: The Contractor will be responsible for making copies, for the Contractors own use and for use by its subcontractors and suppliers.

1.09 SHOP DRAWINGS

- A. Provide shop drawings in the format required by the specifications. Show the information, dimensions, connections and other details necessary to insure that the shop drawings accurately interpret the Contract Documents. Show adjoining construction in such detail as required indicating proper connections. Where adjoining connected construction requires shop drawings or product data, submit such information for approval at the same time so that connections can be accurately checked.

- B. Have shop drawings prepared by a qualified detailer. Shop drawings shall be neatly drawn and clearly legible. Machine duplicated copies of Contract Drawings will not be accepted as shop drawings.
 - 1. Where shop drawings are indicated to be drawn to scale:
 - a. Use scale normally found on an “Architect” or “Engineer” scale.
 - b. Written Scale: Clearly label scales being used on each drawing and/or on each detail on the drawing.
 - 1) Examples: 1/8” = 1’-0” 1” = 40’-0”.
 - c. Graphic Scale: Adjacent to each Written Scale, provide a graphic scale delineating the scale being used. Graphic scale shall be divided into measuring units relating to the accuracy required for the drawing or details.
 - d. Clearly dimension key elements of the drawing or detail.
 - 2. When the drawing sheet is printed full size, the minimum text size shall be 1/8" (3.2 mm) for hand drafting and 3/32" (2.5 mm) for CADD drawings.
- C. Submit the shop drawings through the Submittals Website. The shop drawings will be reviewed and the review results will be posted on the Submittals Website. Contractor will receive email notice of completed review. If the review results in disposition of “DISAPPROVED” or “RETURNED FOR CORRECTION”, promptly correct the deficiencies and resubmit the shop drawings meeting Contract requirements.

1.10 PRODUCT DATA

- A. Provide product data in the format required by the specifications. Modify product data by deleting information that is not applicable to the project or by marking the product data to identify pertinent products. Supplement standard information, if necessary, to provide additional information applicable to project.
- B. Submit the product data through the Submittals Website. The product data will be reviewed and the review results will be posted on the Submittals Website. Contractor will receive email notice of completed review. If the review results in disposition of “DISAPPROVED” or “RETURNED FOR CORRECTION”, promptly correct the deficiencies and resubmit the product data meeting Contract requirements.

1.11 QUALITY ASSURANCE

- A. Provide quality assurance information in the format required by the specifications, including supporting documentation as required.
- B. Submit the quality assurance information through the Submittals Website. The quality assurance information will be reviewed and the review results will be posted on the Submittals Website. Contractor will receive email notice of completed review. If the review results in disposition of “DISAPPROVED” or “RETURNED FOR CORRECTION”, promptly correct the deficiencies and resubmit the quality assurance information meeting Contract requirements.

1.12 SAMPLES

- A. Submit 2 (unless a different number is specified) of each sample required by the Specifications.
- B. Samples will become the property of the State when submitted and will not be incorporated in the Work unless specifically stated otherwise.
- C. The electronic submittal process is not intended for color samples, color charts, or physical material samples.
- D. Record transmittal of each sample required by the Specifications through the Submittals Website.
- E. Consult with the Director's Representative for direction on where Samples will be sent for review.
- F. The sample will be reviewed and the review results will be posted on the Submittals Website. Contractor will receive email notice of completed review.

1.13 REVIEW OF SUBMITTALS

- A. Items submitted for review will be reviewed for compliance with the contract documents, based upon the information submitted. The items will be acted upon with the following dispositions:
 1. Approved (or Reviewed): Where the submittal is marked "Reviewed", the work covered by the submittal may proceed provided it complies with the contract documents. Final acceptance will depend on that compliance.
 2. Approved as Noted (or Reviewed as Modified): Where the submittal is marked "Reviewed as Modified", the work covered by the submittal may proceed provided it complies with the review comments noted on the submittal and the contract documents. Final acceptance will depend on that compliance.
 3. Disapproved (or Revise and Resubmit): Where the submittal is marked "Revise and Resubmit", do not proceed with the work covered by the submittal, including purchasing, fabrication, delivery or other activity for the item submitted. Prepare a new submittal according to the review comments noted on the submittal and meeting the contract documents.
 4. Returned for Correction (or Revise and Resubmit): Where the submittal is marked "Revise and Resubmit", do not proceed with the work covered by the submittal, including purchasing, fabrication, delivery or other activity for the item submitted. Revise or prepare a new submittal according to the review comments noted on the submittal and meeting the contract documents.
 5. Acknowledged (or Received/No Action Required): Where the submittal is marked "Received/No Action Required", receipt of the submittal is acknowledged and has been recorded.
 6. No Action (or Not Reviewed): Where the submittal is marked "Not Reviewed", no review was made of this item, see comments noted on submittal and take appropriate action.

7. Multi-Action: Where the submittal is marked in more than one category, separate dispositions were made for the items submitted, see the review comments for the disposition of each item submitted.

1.14 SCHEDULES AND RECORDS

- A. Submit the following Schedules and Records information not later than 15 days after approval of the Contract unless the Contractor or the Director determines an earlier submission is required to properly schedule or progress the Work.
 1. SCHEDULE OF SUBMITTALS: In the Submittal Log on the Submittals Website, identify long lead items and critical submittals, for each item to be submitted indicate in the "Date Expected" column the date the item will be submitted for review and approval. The submission date that is entered shall provide sufficient time for the item to be reviewed, ordered, delivered and installed for timely completion of the Work in accordance with the Project Schedule. The date entered for submittal of each item is the last day a deviation will be considered.

1.15 TRANSMITTALS

- A. Submittal Transmittal (Form BDC 42):
 1. Furnish separate Form BDC 42 for each submitted item sent to Submittals Website for review.
 - a. Contractor may utilize their own Transmittal Form (or Transmittal Letter) in lieu of utilizing the Form BDC 42, contingent on the Contractor's Transmittal Form includes all information and certifications required by Form BDC 42.
 2. Clearly identify applicable specification section number of submitted item (product data, shop drawing, etc.) on the Form BDC 42.
 3. Transmit items designated in the Schedule of Submittals (and project specifications) to the Submittals Website.

PART 2 PRODUCTS (Not Used)

PART 3 EXECUTION (Not Used)

END OF SECTION



Design and Construction

AN ISO 9001:2008 CERTIFIED ORGANIZATION

Division of Construction, 34th Floor, Corning Tower
The Governor Nelson A. Rockefeller Empire State Plaza
Albany, New York 12242

Phone: (518) 474-0331 FAX: (518) 474-8201

SUBMITTAL TRANSMITTAL

Project No.: _____

NOTE: A Transmittal is required for each Specification Section. DO NOT bind together separate submittals from different Specification Sections.

This form is to be used *only* if there are no deviations from the Contract Documents. If there are ANY deviations from the Contract Documents, you must submit the Contract Document Deviation Request Form (BDC 49).

Project Description: *(Project Title, Facility Name and Address)*

Date: _____

TO:

FROM:

SUBMITTAL TYPE:

- | | | |
|---------------------------------------|--|--|
| <input type="checkbox"/> Product Data | <input type="checkbox"/> Re-Submittal | <input type="checkbox"/> Information (Waiver) |
| <input type="checkbox"/> Test Reports | <input type="checkbox"/> Shop Drawings | <input type="checkbox"/> Quality Control/Assurance |
| <input type="checkbox"/> Design Data | <input type="checkbox"/> Certificate | <input type="checkbox"/> Contract Closeout |
| | <input type="checkbox"/> Samples | <input type="checkbox"/> Other |

Comply with all submittal requirements in the Project Manual as per Section 013300 and the particular Specification Section for which you are transmitting material.

Specification Number and Title: _____

Part	Type	Description

Contractor's Certification:

We have verified that all material or equipment contained in this submittal meets all the requirements specified or shown **(no exceptions)**.

Contractor/Contractor's Representative (Print Name)

Signature



NYS OGS DESIGN AND CONSTRUCTION SUBMITTAL COMMENTS

To: Contractor: **Submittal No.:**
From: EIC:
Contract No.: Submittal Desc:
Facility: Disposition:
Reviewed By: Remarks:

No.	Date of Action	Action	Spec Section	Supplier/Mfr	No. of Dwgs	Drawing No's
-----	----------------	--------	--------------	--------------	-------------	--------------

1

Item Description:

Remarks:

2

Item Description:

Remarks:

3

Item Description:

Remarks:



Request for Information

Design And Construction
 Division of Construction
 34th Floor, Corning Tower
 The Governor Nelson A. Rockefeller
 Empire State Plaza
 Albany, New York 12242
 FAX: (518)474-8201

Project Information		
Project Number	Client	Location
	Project Title	
RFI Information		
Number	Trades	Spec Section
Contractor's Ref#		Drawing No.
Brief Description		
Date of Request	Requested By	Affiliation
	Estimated Cost Impact <input type="checkbox"/> Additional Cost <input type="checkbox"/> No Change <input type="checkbox"/> Credit	
Detailed Description		
Response Date	Response By	Affiliation
	Estimated Cost Impact <input type="checkbox"/> Additional Cost <input type="checkbox"/> No Change <input type="checkbox"/> Credit	
Response		
Attached Document Description		



Design and Construction

AN ISO 9001:2008 CERTIFIED ORGANIZATION


Division of Construction, 34th Floor, Corning Tower
The Governor Nelson A. Rockefeller Empire State Plaza
Albany, New York 12242

Phone: (518) 474-0331 FAX: (518) 474-8201


INFORMATION BULLETIN

Project No.: _____

Project Description: <i>(Project Title, Facility Name and Address)</i>			Client Agency:		
IB No.:	Trades:	Spec. Section:		Drawing No.:	
Brief Description:					
Issue Date:	Issued By:		Affiliation:		
Detailed Description:					
Justification:					
Estimated Cost Impact: <input type="checkbox"/> Additional Cost <input type="checkbox"/> No Change <input type="checkbox"/> Credit			Estimated Time Impact: <input type="checkbox"/> YES <input type="checkbox"/> NO		
Attached Document Description:					

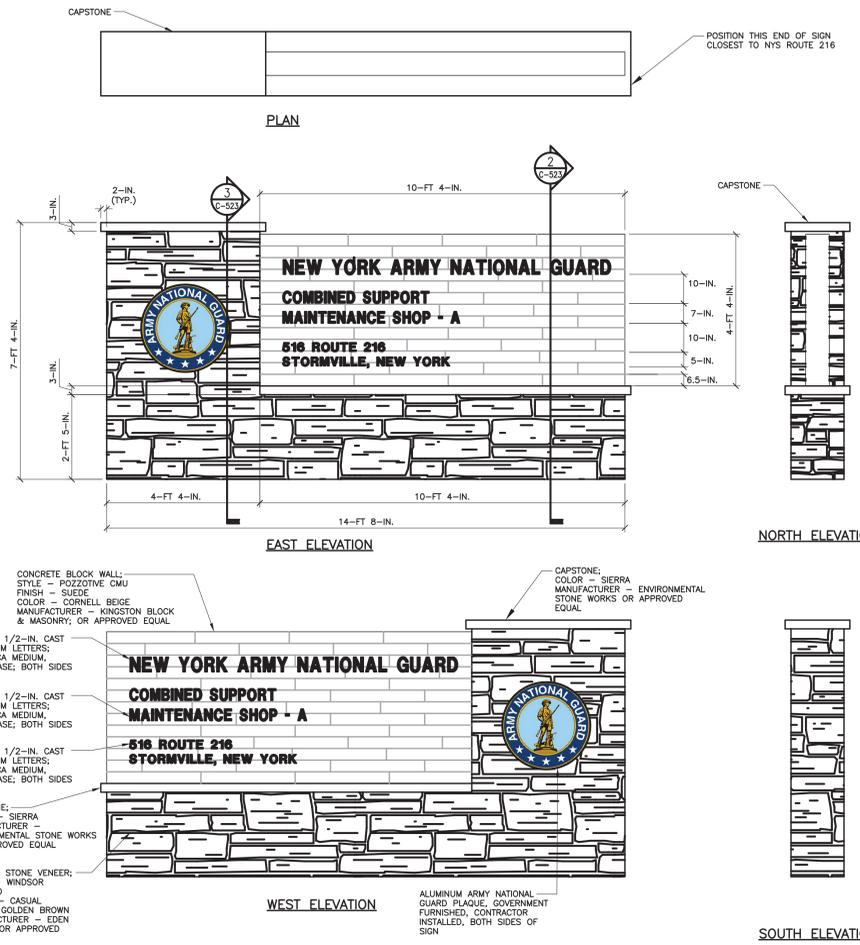


1 FACILITY SIGN PLAN AND ELEVATION DETAILS
C-524 NO SCALE

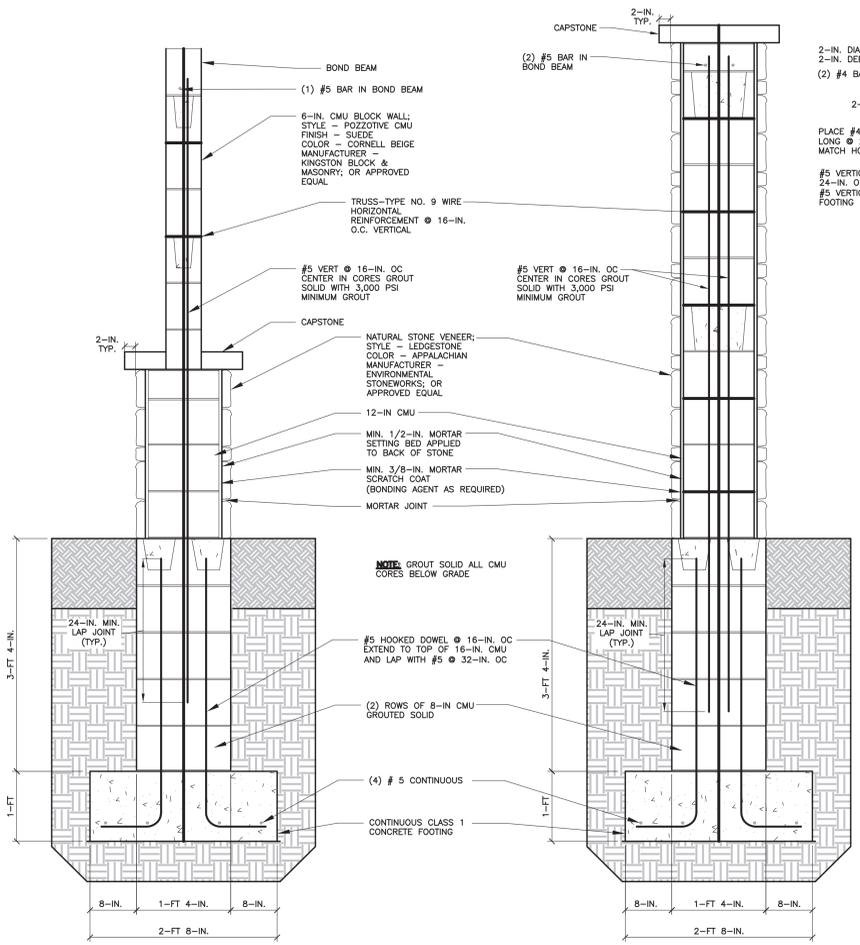


2 FACILITY SIGN SECTION
C-524 NO SCALE


3 FACILITY SIGN SECTION
C-524 NO SCALE




4 CAPSTONE DETAIL
C-524 NO SCALE

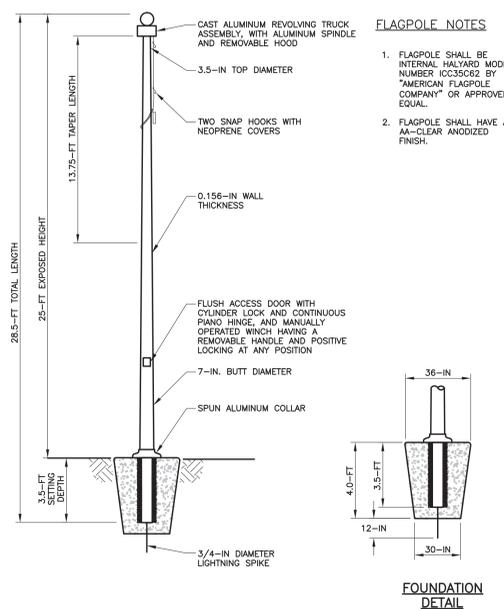


5 FLAG POLE DETAIL
C-524 NO SCALE

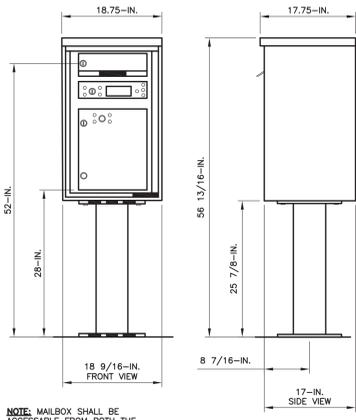


6 MAILBOX DETAIL
C-524 NO SCALE

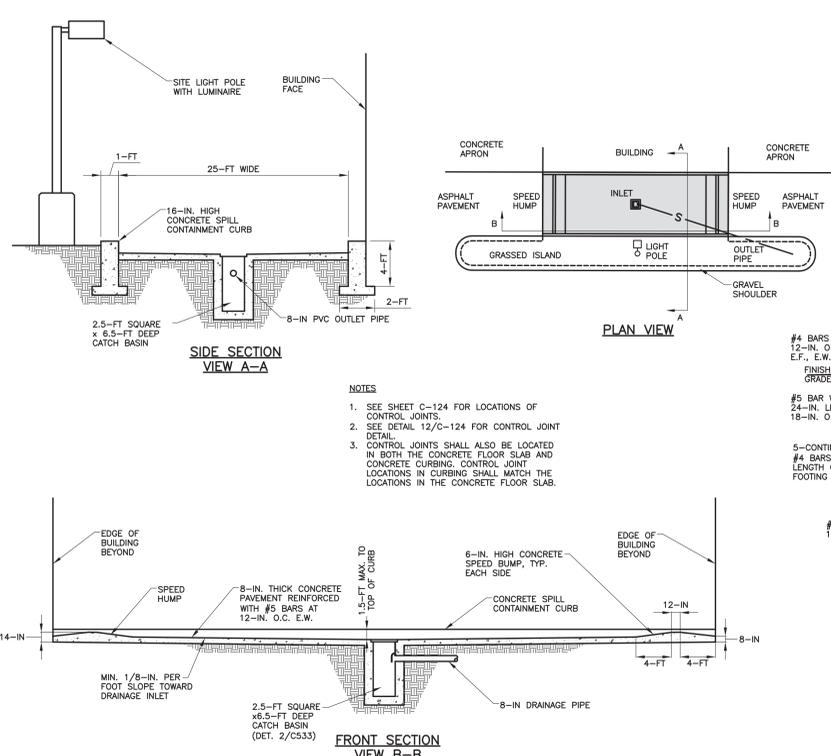

7 EXTERIOR WASHOUT BAY DETAILS
C-524 NO SCALE

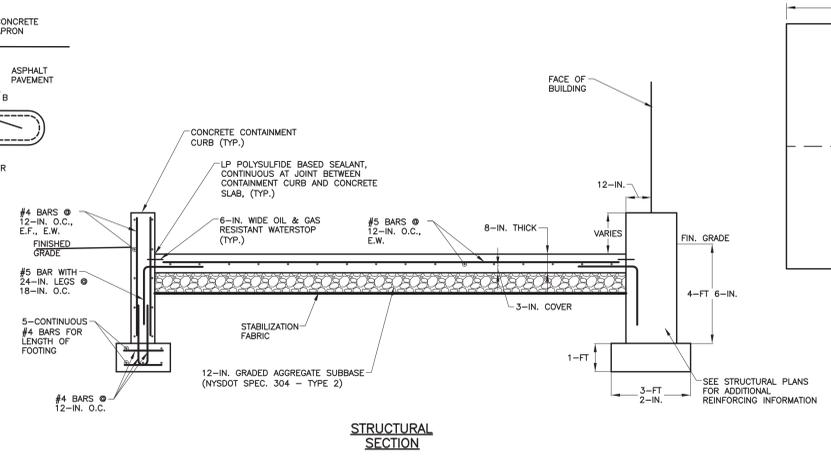

STRUCTURAL SECTION

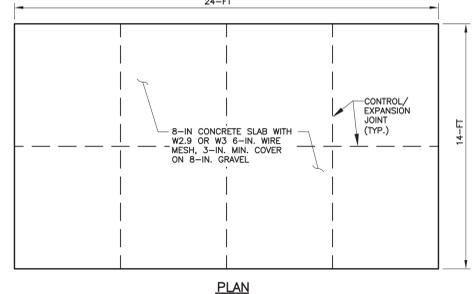

THICKENED EDGE DETAIL

8 ARTIFACT DISPLAY PAD DETAILS
C-524 NO SCALE

WARNING:
THE ALTERATION OF THE MATERIAL IN ANY WAY, UNLESS DONE UNDER THE DIRECTION OF A COMPARABLE PROFESSIONAL, IS ARCHITECTURE FOR AN ARCHITECT, ENGINEER OR PROFESSIONAL LANDSCAPE ARCHITECT FOR A LANDSCAPE ARCHITECT IS A VIOLATION OF THE NEW YORK STATE EDUCATION LAW AND/OR REGULATIONS AND IS A CLASS B MISDEMEANOR.



CONTRACT: **CONSTRUCTION**

TITLE: **PROVIDE COMBINED SUPPORT MAINTENANCE SHOP**

LOCATION: **STORMVILLE CSMS
516 - ROUTE 216
STORMVILLE, NEW YORK**

CLIENT: **DIVISION OF MILITARY AND NAVAL AFFAIRS**

MARK	DATE	DESCRIPTION
PROJECT NUMBER:	OGS No. 44362 - C	PRIDE No. 360139
DESIGNED BY:	RJY	
DRAWN BY:	RJY	
FIELD CHECK:		
APPROVED:	AKL	
SHEET TITLE:	SITE DETAILS SHEET 5	

COMBINED SUPPORT MAINTENANCE SHOP

516 ROUTE 216

STORMVILLE, NEW YORK


OGS PROJECT No. 44362 - CONSTRUCTION

MILCON PRIDE PROJECT No. 360139

VOLUME 1 OF 2



VICINITY MAP

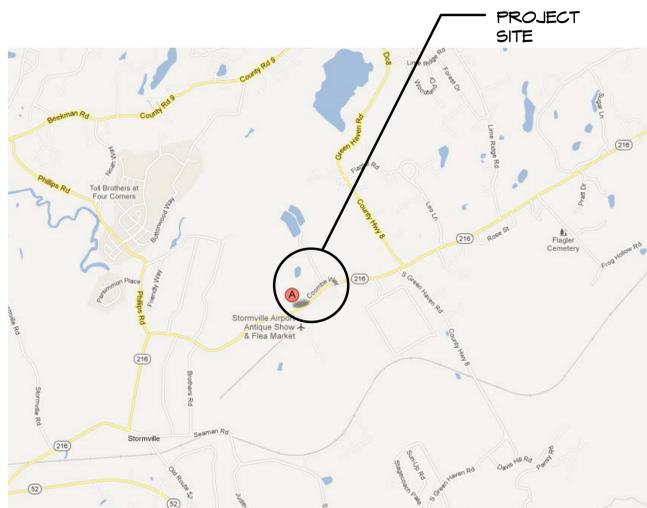

LOCATION MAP

VOLUME 1

CIVIL DRAWINGS

- V-001 REFERENCE DRAWING
- V-002 REFERENCE DRAWING
- C-001 SITE LEGENDS AND ABBREVIATIONS
- C-101 GENERAL PLAN AND SURVEY CONTROL
- C-102 KEY MAP AND NOTES
- C-103 OVERALL SITE PLAN
- C-104 PHASING AND STAGING PLAN
- C-105 PHASING AND STAGING PLAN
- C-110 EXISTING CONDITIONS AND CLEARING PLAN
- C-120 SITE PLAN (ZONE 1)
- C-121 SITE PLAN (ZONE 2)
- C-122 SITE PLAN (ZONE 3)
- C-123 SITE PLAN (ZONE 4)
- C-124 CONCRETE APRON REINFORCING AND JOINTING PLAN
- C-125 ALTERNATE BID ITEMS
- C-130 UTILITY PLAN (ZONE 1)
- C-131 UTILITY PLAN (ZONE 2)
- C-132 UTILITY PLAN (ZONE 3)
- C-133 UTILITY PLAN (ZONE 4)
- C-134 UTILITY PLAN (ZONE 5)
- C-135 UTILITY PLAN (ZONE 6)
- C-136 UTILITY PLAN (ZONE 7)
- C-137 UTILITY PLAN (ZONE 8)
- C-140 GRADING PLAN (ZONE 1)
- C-141 GRADING PLAN (ZONE 2)
- C-142 GRADING PLAN (ZONE 3)
- C-143 GRADING PLAN (ZONE 4)
- C-144 GRADING PLAN (ZONE 9)
- C-145 EROSION CONTROL PLAN (ZONE 1)
- C-146 EROSION CONTROL PLAN (ZONE 2)
- C-147 EROSION CONTROL PLAN (ZONE 3)
- C-148 EROSION CONTROL PLAN (ZONE 4)
- C-150 CONSTRUCTION COORDINATE PLAN (ZONE 1)
- C-151 CONSTRUCTION COORDINATE PLAN (ZONE 2)
- C-152 CONSTRUCTION COORDINATE PLAN (ZONE 3)
- C-153 CONSTRUCTION COORDINATE PLAN (ZONE 4)
- C-154 CONSTRUCTION COORDINATE TABLES
- C-160 SIGN LOCATION AND PAVEMENT MARKING PLAN (ZONE 1)
- C-161 SIGN LOCATION AND PAVEMENT MARKING PLAN (ZONE 2)
- C-162 SIGN LOCATION AND PAVEMENT MARKING PLAN (ZONE 3)
- C-163 SIGN LOCATION AND PAVEMENT MARKING PLAN (ZONE 4)
- C-164 SIGN DATA SHEET
- C-170 PLANTING SCHEDULE
- C-230 STRUCTURE TABLES
- C-231 STORM SEWER PROFILES
- C-232 STORM SEWER PROFILES
- C-233 SANITARY SEWER PROFILES
- C-234 WATER MAIN PROFILES
- C-235 WATER MAIN PROFILES 2
- C-236 WATER MAIN PROFILES 3
- C-520 SITE DETAILS - SHEET 1
- C-521 SITE DETAILS - SHEET 2
- C-522 SITE DETAILS - SHEET 3
- C-523 SITE DETAILS - SHEET 4
- C-524 SITE DETAILS - SHEET 5
- C-530 UTILITY DETAILS - WATER DISTRIBUTION AND FIRE PROTECTION
- C-531 UTILITY DETAILS - SANITARY SEWER
- C-532 UTILITY DETAILS - STORMWATER
- C-533 UTILITY DETAILS - STORMWATER
- C-540 EROSION CONTROL DETAILS AND SWPPP NOTES
- C-541 MAINTENANCE AND PROTECTION OF TRAFFIC

STRUCTURAL DRAWINGS

- S-000 GENERAL NOTES AND DESIGN CRITERIA
- S-100 FOUNDATION PLAN - AREA 'A'
- S-101 FOUNDATION PLAN - AREA 'B'
- S-102 FOUNDATION PLAN - AREA 'C'
- S-103 SECOND FLOOR (AREA 'A'), EQUIPMENT PLATFORM (AREA 'C') & PART ROOF PLAN
- S-104 ROOF FRAMING PLAN - AREA 'A'
- S-105 ROOF FRAMING PLAN - AREA 'B'
- S-106 ROOF FRAMING PLAN - AREA 'C'
- S-107 PARTIAL ROOF FRAMING PLAN AT THE RIDGE OF TRUSS - AREAS 'B' & 'C'
- S-108 PLAN AT CRANE GIRDER LEVEL - AREA 'B' & AREA 'C'
- S-109 FOUNDATION AND ROOF FRAMING PLAN - AREA 'D'
- S-109A FOUNDATION AND ROOF FRAMING - AREA 'E' ALTERNATE #3
- S-200 TRUSS BOTTOM CHORD BRACING PLAN - AREA 'B' AND DETAILS
- S-201 VERTICAL BRACING ELEVATIONS - AREA 'B'
- S-202 TRUSS BOTTOM CHORD BRACING PLAN - AREA 'C'
- S-203 VERTICAL BRACING ELEVATIONS - AREA 'C'
- S-204 TYPICAL SAG ROD ELEVATION AND DETAILS

INDEX OF DRAWINGS

STRUCTURAL DRAWINGS CONTINUED

- S-500 TYPICAL TRUSS PROFILES FOR WORK BAYS - AREA 'B' & DETAILS
- S-501 TYPICAL TRUSS PROFILES FOR WORK BAY - AREA 'C'
- S-502 SECTIONS AND DETAILS FOR CRANE GIRDER
- S-503 NOT USED
- S-504 TYPICAL FOUNDATION DETAILS
- S-505 TYPICAL DETAILS
- S-506 LATERAL SUPPORT DETAILS FOR GABLE END AND INTERIOR WALLS
- S-507 SECTIONS & DETAILS
- S-508 SECTIONS & DETAILS
- S-509 SECTIONS & DETAILS
- S-510 SECTIONS & DETAILS
- S-600 COLUMN SCHEDULE
- S-601 SECTIONS & DETAILS
- S-602 SECTIONS & DETAILS
- S-700 AREA 'D' & 'E' SECTION AND DETAILS
- S-701 AREA 'D' & 'E' SECTION AND DETAILS

ARCHITECTURAL DRAWINGS

- A-001 ABBREVIATIONS, SYMBOL KEY AND WALL PARTITION LEGEND
- A-100 CODE COMPLIANCE PLANS
- A-101 FIRST FLOOR PLAN - AREA 'A'
- A-102 FIRST FLOOR PLAN - AREA 'B'
- A-103 FIRST FLOOR PLAN - AREA 'C'
- A-104 SECOND FLOOR PLAN - AREA 'A' & 'C'
- A-105 ROOF PLAN
- A-106 FLOOR PLANS AND ELEVATIONS - AREA 'D'
- A-107 FLOOR PLANS AND ELEVATIONS - AREA 'E' - ALTERNATE #3
- A-200 EXTERIOR ELEVATIONS
- A-201 EXTERIOR ELEVATIONS
- A-300 BUILDING SECTIONS
- A-301 BUILDING SECTIONS
- A-302 WALL SECTIONS
- A-303 WALL SECTIONS
- A-304 WALL SECTIONS
- A-305 WALL SECTIONS
- A-306 WALL SECTIONS
- A-307 WALL SECTIONS
- A-308 WALL SECTIONS
- A-309 WALL SECTIONS
- A-310 WALL SECTIONS
- A-400 DETAILED FLOOR PLANS
- A-401 DETAILED STAIR PLANS AND SECTIONS
- A-402 STAIR SECTIONS, STAIR DETAILS AND LADDER DETAILS
- A-500 TYPICAL INTERIOR WALL DETAILS
- A-501 PLAN DETAILS
- A-502 ROOF DETAILS
- A-503 ROOF DETAILS
- A-504 ROOF DETAILS
- A-505 ROOF DETAILS
- A-600 ROOM FINISH SCHEDULE
- A-601 DOOR SCHEDULE AND TYPES
- A-602 DOOR DETAILS
- A-603 DOOR DETAILS
- A-604 WINDOW TYPES AND DETAILS
- A-605 WINDOW TYPES AND DETAILS
- A-700 ADA COMPLIANCE
- A-701 INTERIOR ELEVATIONS
- A-702 INTERIOR ELEVATIONS
- A-703 FURNITURE & EQUIPMENT PLAN - AREA 'A'
- A-704 FURNITURE & EQUIPMENT PLAN - AREA 'B'
- A-705 FURNITURE & EQUIPMENT PLAN - AREA 'C'
- A-800 FIRST FLOOR REFLECTED CEILING PLAN - AREA 'A'
- A-801 FIRST FLOOR REFLECTED CEILING PLAN - AREA 'B'
- A-802 FIRST FLOOR REFLECTED CEILING PLAN - AREA 'C'
- A-803 REFLECTED CEILING PLAN DETAILS
- A-900 3D PERSPECTIVES

VOLUME 2

PLUMBING DRAWINGS

- P-000 LEGENDS AND SCHEDULES
- P-100 FIRST FLOOR PLAN AREA 'A' SANITARY
- P-101 FIRST FLOOR PLAN AREA 'B' SANITARY
- P-102 FIRST FLOOR PLAN AREA 'C' SANITARY
- P-103 FIRST FLOOR AREA 'A' SUPPLY
- P-104 FIRST FLOOR AREA 'B' SUPPLY
- P-105 FIRST FLOOR AREA 'C' SUPPLY
- P-106 FIRST FLOOR POL AND COMPRESSED AIR
- P-107 SECOND FLOOR PLAN AND DETACHED BUILDING
- P-108 ROOF PLAN
- P-109 SITE PLAN
- P-301 PLUMBING DETAILS
- P-302 PLUMBING DETAILS
- P-303 POL AND COMPRESSED AIR SCHEMATIC

HVAC DRAWINGS

- H-000 LEGEND
- H-001 SCHEDULES
- H-002 SCHEDULES
- H-100 FIRST FLOOR AREA 'A' - DUCTWORK / EQUIPMENT
- H-101 FIRST FLOOR AREA 'B' - DUCTWORK / EQUIPMENT
- H-102 FIRST FLOOR AREA 'C' - DUCTWORK / EQUIPMENT
- H-103 OUTBUILDING, AREA 'E' - ALTERNATE #3
- H-200 FIRST FLOOR AREA 'A' PIPING/EQUIPMENT
- H-201 FIRST FLOOR AREA 'B' - PIPING / EQUIPMENT
- H-202 FIRST FLOOR AREA 'C' - PIPING / EQUIPMENT AND AREA 'D'
- H-300 SECOND FLOOR MECHANICAL ROOM
- H-301 EQUIPMENT PLATFORM
- H-302 BOILER ROOM
- H-400 SECTIONS
- H-500 DETAILS
- H-501 DETAILS
- H-502 DETAILS
- H-503 DETAILS
- H-600 CONTROLS
- H-601 CONTROLS

ELECTRICAL DRAWINGS

- E-000 ABBREVIATIONS, LEGEND, AND GENERAL NOTES
- E-001 ONELINE DIAGRAM
- E-002 SITE LIGHTING PLAN
- E-003 SITE POWER AND CONDUIT RUN PLAN
- E-004 PANEL SCHEDULES
- E-005 PANEL SCHEDULES
- E-006 SCHEDULES
- E-100 FIRST FLOOR PLAN AREA 'A' - POWER INSTALLATION
- E-101 FIRST FLOOR PLAN AREA 'B' - POWER INSTALLATION
- E-102 FIRST FLOOR PLAN AREA 'C' - POWER INSTALLATION
- E-103 2ND FLOOR PLAN AREA 'A' & 'C' - POWER INSTALLATION
- E-200 FIRST FLOOR PLAN AREA 'A' - LIGHTING INSTALLATION
- E-201 FIRST FLOOR PLAN AREA 'A' - LIGHTING INSTALLATION
- E-202 FIRST FLOOR PLAN AREA 'C' - LIGHTING INSTALLATION
- E-203 2ND FLOOR PLAN AREA 'A' & 'C' - LIGHTING INSTALLATION AND DAYLIGHTING ONE-LINE DETAIL
- E-300 FIRST FLOOR PLAN AREA 'A' - COMMUNICATIONS & DATA
- E-301 FIRST FLOOR PLAN AREA 'B' - COMMUNICATIONS & DATA
- E-302 FIRST FLOOR PLAN AREA 'C' - COMMUNICATIONS & DATA
- E-303 DATA RISER DIAGRAM
- E-304 DETAILS & LEGEND SHEET
- E-400 FIRST FLOOR PLAN AREA 'A' - FIRE ALARM INSTALLATION
- E-401 FIRST FLOOR PLAN AREA 'B' - FIRE ALARM INSTALLATION
- E-402 FIRST FLOOR PLAN AREA 'C' - FIRE ALARM INSTALLATION
- E-403 2ND FLOOR PLAN AREA 'A' & 'C' - FIRE ALARM INSTALLATION & TYPICAL FIRE ALARM RISERS
- E-500 FIRST FLOOR PLAN AREA 'A' - SECURITY INSTALLATION
- E-600 OUTBUILDING AREA 'D' AND GREENHAVEN CORRECTIONAL FACILITY
- E-601 OUTBUILDINGS AREA 'E', ALTERNATE #3
- E-700 LIGHTNING PROTECTION AND HEAT TRACE
- E-701 LIGHTNING PROTECTION DETAILS
- E-800 DETAILS
- E-801 DETAILS
- E-802 DETAILS
- E-803 DETAILS
- E-804 INTERIOR ELEVATIONS



ANDREW M. CUOMO
Governor
ROANN M. DESTITO
Commissioner

06-11-2013

G-001

REVISED DATE: 8-5-13

COMBINED SUPPORT MAINTENANCE SHOP

516 ROUTE 216

STORMVILLE, NEW YORK


OGS PROJECT No. 44362 - CONSTRUCTION

MILCON PRIDE PROJECT No. 360139

VOLUME 2 OF 2



VICINITY MAP

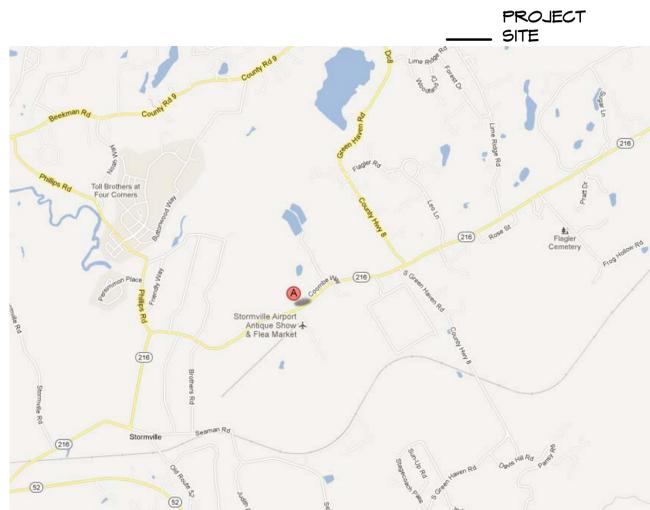

LOCATION MAP

VOLUME 1

CIVIL DRAWINGS

- V-001 REFERENCE DRAWING
- V-002 REFERENCE DRAWING
- C-001 SITE LEGENDS AND ABBREVIATIONS
- C-101 GENERAL PLAN AND SURVEY CONTROL KEY MAP AND NOTES
- C-102 OVERALL SITE PLAN
- C-104 PHASING AND STAGING PLAN
- C-105 PHASING AND STAGING PLAN
- C-110 EXISTING CONDITIONS AND CLEARING PLAN
- C-120 SITE PLAN (ZONE 1)
- C-121 SITE PLAN (ZONE 2)
- C-122 SITE PLAN (ZONE 3)
- C-123 SITE PLAN (ZONE 4)
- C-124 CONCRETE APRON REINFORCING AND JOINTING PLAN
- C-125 ALTERNATE BID ITEMS
- C-130 UTILITY PLAN (ZONE 1)
- C-131 UTILITY PLAN (ZONE 2)
- C-132 UTILITY PLAN (ZONE 3)
- C-133 UTILITY PLAN (ZONE 4)
- C-134 UTILITY PLAN (ZONE 5)
- C-135 UTILITY PLAN (ZONE 6)
- C-136 UTILITY PLAN (ZONE 7)
- C-137 UTILITY PLAN (ZONE 8)
- C-140 GRADING PLAN (ZONE 1)
- C-141 GRADING PLAN (ZONE 2)
- C-142 GRADING PLAN (ZONE 3)
- C-143 GRADING PLAN (ZONE 4)
- C-144 GRADING PLAN (ZONE 9)
- C-145 EROSION CONTROL PLAN (ZONE 1)
- C-146 EROSION CONTROL PLAN (ZONE 2)
- C-147 EROSION CONTROL PLAN (ZONE 3)
- C-148 EROSION CONTROL PLAN (ZONE 4)
- C-150 CONSTRUCTION COORDINATE PLAN (ZONE 1)
- C-151 CONSTRUCTION COORDINATE PLAN (ZONE 2)
- C-152 CONSTRUCTION COORDINATE PLAN (ZONE 3)
- C-153 CONSTRUCTION COORDINATE PLAN (ZONE 4)
- C-154 CONSTRUCTION COORDINATE TABLES
- C-160 SIGN LOCATION AND PAVEMENT MARKING PLAN (ZONE 1)
- C-161 SIGN LOCATION AND PAVEMENT MARKING PLAN (ZONE 2)
- C-162 SIGN LOCATION AND PAVEMENT MARKING PLAN (ZONE 3)
- C-163 SIGN LOCATION AND PAVEMENT MARKING PLAN (ZONE 4)
- C-164 SIGN DATA SHEET
- C-170 PLANTING SCHEDULE
- C-230 STRUCTURE TABLES
- C-231 STORM SEWER PROFILES
- C-232 SANITARY SEWER PROFILES
- C-234 WATER MAIN PROFILES
- C-235 WATER MAIN PROFILES 2
- C-236 WATER MAIN PROFILES 3
- C-520 SITE DETAILS - SHEET 1
- C-521 SITE DETAILS - SHEET 2
- C-522 SITE DETAILS - SHEET 3
- C-523 SITE DETAILS - SHEET 4
- C-524 SITE DETAILS - SHEET 5
- C-530 UTILITY DETAILS - WATER DISTRIBUTION AND FIRE PROTECTION
- C-531 UTILITY DETAILS - SANITARY SEWER
- C-532 UTILITY DETAILS - STORMWATER
- C-533 UTILITY DETAILS - STORMWATER
- C-540 EROSION CONTROL DETAILS AND SWPPP NOTES
- C-541 MAINTENANCE AND PROTECTION OF TRAFFIC

STRUCTURAL DRAWINGS

- S-000 GENERAL NOTES AND DESIGN CRITERIA
- S-100 FOUNDATION PLAN - AREA 'A'
- S-101 FOUNDATION PLAN - AREA 'B'
- S-102 FOUNDATION PLAN - AREA 'C'
- S-103 SECOND FLOOR (AREA 'A'), EQUIPMENT PLATFORM (AREA 'C') & PART ROOF PLAN
- S-104 ROOF FRAMING PLAN - AREA 'A'
- S-105 ROOF FRAMING PLAN - AREA 'B'
- S-106 ROOF FRAMING PLAN - AREA 'C'
- S-107 PARTIAL ROOF FRAMING PLAN AT THE RIDGE OF TRUSS - AREAS 'B' & 'C'
- S-108 PLAN AT CRANE GIRDER LEVEL - AREA 'B' & AREA 'C'
- S-109 FOUNDATION AND ROOF FRAMING PLAN - AREA 'D'
- S-109A FOUNDATION AND ROOF FRAMING - AREA 'E' ALTERNATE #3
- S-200 TRUSS BOTTOM CHORD BRACING PLAN - AREA 'B' AND DETAILS
- S-201 VERTICAL BRACING ELEVATIONS - AREA 'B'
- S-202 TRUSS BOTTOM CHORD BRACING PLAN - AREA 'C'
- S-203 VERTICAL BRACING ELEVATIONS - AREA 'C'
- S-204 TYPICAL SAG ROD ELEVATION AND DETAILS

INDEX OF DRAWINGS

STRUCTURAL DRAWINGS CONTINUED

- S-500 TYPICAL TRUSS PROFILES FOR WORK BAYS - AREA 'B' & DETAILS
- S-501 TYPICAL TRUSS PROFILES FOR WORK BAY - AREA 'C'
- S-502 SECTIONS AND DETAILS FOR CRANE GIRDER
- S-503 NOT USED
- S-504 TYPICAL FOUNDATION DETAILS
- S-505 TYPICAL DETAILS
- S-506 LATERAL SUPPORT DETAILS FOR GABLE END AND INTERIOR WALLS
- S-507 SECTIONS & DETAILS
- S-508 SECTIONS & DETAILS
- S-509 SECTIONS & DETAILS
- S-510 SECTIONS & DETAILS
- S-600 COLUMN SCHEDULE
- S-601 SECTIONS & DETAILS
- S-602 SECTIONS & DETAILS
- S-700 AREA 'D' & 'E' SECTION AND DETAILS
- S-701 AREA 'D' & 'E' SECTION AND DETAILS

ARCHITECTURAL DRAWINGS

- A-001 ABBREVIATIONS, SYMBOL KEY AND WALL PARTITION LEGEND
- A-100 CODE COMPLIANCE PLANS
- A-101 FIRST FLOOR PLAN - AREA 'A'
- A-102 FIRST FLOOR PLAN - AREA 'B'
- A-103 FIRST FLOOR PLAN - AREA 'C'
- A-104 SECOND FLOOR PLAN - AREA 'A' & 'C'
- A-105 ROOF PLAN
- A-106 FLOOR PLANS AND ELEVATIONS - AREA 'D'
- A-107 FLOOR PLANS AND ELEVATIONS - AREA 'E' - ALTERNATE #3
- A-200 EXTERIOR ELEVATIONS
- A-201 EXTERIOR ELEVATIONS
- A-300 BUILDING SECTIONS
- A-301 BUILDING SECTIONS
- A-302 WALL SECTIONS
- A-303 WALL SECTIONS
- A-304 WALL SECTIONS
- A-305 WALL SECTIONS
- A-306 WALL SECTIONS
- A-307 WALL SECTIONS
- A-308 WALL SECTIONS
- A-309 WALL SECTIONS
- A-310 WALL SECTIONS
- A-400 DETAILED FLOOR PLANS
- A-401 DETAILED STAIR PLANS AND SECTIONS
- A-402 STAIR SECTIONS, STAIR DETAILS AND LADDER DETAILS
- A-500 TYPICAL INTERIOR WALL DETAILS
- A-501 PLAN DETAILS
- A-502 ROOF DETAILS
- A-503 ROOF DETAILS
- A-504 ROOF DETAILS
- A-505 ROOF DETAILS
- A-600 ROOM FINISH SCHEDULE
- A-601 DOOR SCHEDULE AND TYPES
- A-602 DOOR DETAILS
- A-603 DOOR DETAILS
- A-604 WINDOW TYPES AND DETAILS
- A-605 WINDOW TYPES AND DETAILS
- A-700 ADA COMPLIANCE
- A-701 INTERIOR ELEVATIONS
- A-702 INTERIOR ELEVATIONS
- A-703 FURNITURE & EQUIPMENT PLAN - AREA 'A'
- A-704 FURNITURE & EQUIPMENT PLAN - AREA 'B'
- A-705 FURNITURE & EQUIPMENT PLAN - AREA 'C'
- A-800 FIRST FLOOR REFLECTED CEILING PLAN - AREA 'A'
- A-801 FIRST FLOOR REFLECTED CEILING PLAN - AREA 'B'
- A-802 FIRST FLOOR REFLECTED CEILING PLAN - AREA 'C'
- A-803 REFLECTED CEILING PLAN DETAILS
- A-900 3D PERSPECTIVES

VOLUME 2

PLUMBING DRAWINGS

- P-000 LEGENDS AND SCHEDULES
- P-100 FIRST FLOOR PLAN AREA 'A' SANITARY
- P-101 FIRST FLOOR PLAN AREA 'B' SANITARY
- P-102 FIRST FLOOR PLAN AREA 'C' SANITARY
- P-103 FIRST FLOOR AREA 'A' SUPPLY
- P-104 FIRST FLOOR AREA 'B' SUPPLY
- P-105 FIRST FLOOR AREA 'C' SUPPLY
- P-106 FIRST FLOOR POL AND COMPRESSED AIR
- P-107 SECOND FLOOR PLAN AND DETACHED BUILDING
- P-108 ROOF PLAN
- P-109 SITE PLAN
- P-301 PLUMBING DETAILS
- P-302 PLUMBING DETAILS
- P-303 POL AND COMPRESSED AIR SCHEMATIC

HVAC DRAWINGS

- H-000 LEGEND
- H-001 SCHEDULES
- H-002 SCHEDULES
- H-100 FIRST FLOOR AREA 'A' - DUCTWORK / EQUIPMENT
- H-101 FIRST FLOOR AREA 'B' - DUCTWORK / EQUIPMENT
- H-102 FIRST FLOOR AREA 'C' - DUCTWORK / EQUIPMENT
- H-103 OUTBUILDING - AREA 'E' - ALTERNATE #3
- H-200 FIRST FLOOR AREA 'A' PIPING/EQUIPMENT
- H-201 FIRST FLOOR AREA 'B' PIPING / EQUIPMENT
- H-202 FIRST FLOOR AREA 'C' PIPING / EQUIPMENT AND AREA 'D'
- H-300 SECOND FLOOR MECHANICAL ROOM
- H-301 EQUIPMENT PLATFORM
- H-302 BOILER ROOM
- H-400 SECTIONS
- H-500 DETAILS
- H-501 DETAILS
- H-502 DETAILS
- H-600 CONTROLS
- H-601 CONTROLS

ELECTRICAL DRAWINGS

- E-000 ABBREVIATIONS, LEGEND, AND GENERAL NOTES
- E-001 ONELINE DIAGRAM
- E-002 SITE LIGHTING PLAN
- E-003 SITE POWER AND CONDUIT RUN PLAN
- E-004 PANEL SCHEDULES
- E-005 PANEL SCHEDULES
- E-006 SCHEDULES
- E-100 FIRST FLOOR PLAN AREA 'A' - POWER INSTALLATION
- E-101 FIRST FLOOR PLAN AREA 'B' - POWER INSTALLATION
- E-102 FIRST FLOOR PLAN AREA 'C' - POWER INSTALLATION
- E-103 2ND FLOOR PLAN AREA 'A' & 'C' - POWER INSTALLATION
- E-200 FIRST FLOOR PLAN AREA 'A' - LIGHTING INSTALLATION
- E-201 FIRST FLOOR PLAN AREA 'B' - LIGHTING INSTALLATION
- E-202 FIRST FLOOR PLAN AREA 'C' - LIGHTING INSTALLATION
- E-203 2ND FLOOR PLAN AREA 'A' & 'C' - LIGHTING INSTALLATION AND DAYLIGHTING ONE-LINE DETAIL
- E-300 FIRST FLOOR PLAN AREA 'A' - COMMUNICATIONS & DATA
- E-301 FIRST FLOOR PLAN AREA 'B' - COMMUNICATIONS & DATA
- E-302 FIRST FLOOR PLAN AREA 'C' - COMMUNICATIONS & DATA
- E-303 DATA RISER DIAGRAM
- E-304 DETAILS & LEGEND SHEET
- E-400 FIRST FLOOR PLAN AREA 'A' - FIRE ALARM INSTALLATION
- E-401 FIRST FLOOR PLAN AREA 'B' - FIRE ALARM INSTALLATION
- E-402 FIRST FLOOR PLAN AREA 'C' - FIRE ALARM INSTALLATION
- E-403 2ND FLOOR PLAN AREA 'A' & 'C' - FIRE ALARM INSTALLATION & TYPICAL FIRE ALARM RISERS
- E-500 FIRST FLOOR PLAN AREA 'A' - SECURITY INSTALLATION
- E-600 OUTBUILDING AREA 'D' AND GREENHAVEN CORRECTIONAL FACILITY
- E-700 OUTBUILDINGS AREA 'E', ALTERNATE #3
- E-700 LIGHTNING PROTECTION AND HEAT TRACE
- E-701 LIGHTNING PROTECTION DETAILS
- E-800 DETAILS
- E-801 DETAILS
- E-802 DETAILS
- E-803 DETAILS
- E-804 INTERIOR ELEVATIONS



ANDREW M. CUOMO
Governor
ROANN M. DESTITO
Commissioner

Serving New York

06-11-2013

G-002

REVISED DATE: 8-5-13
